

**Implementation Status & Results**  
**Brazil**  
**S PAULO METRO LINE 4 (PHASE 2) (P106390)**

Operation Name: S PAULO METRO LINE 4 (PHASE 2) (P106390)	Project Stage: Implementation	Seq.No: 2	Status: ARCHIVED	Last Modified Date: 16-Nov-2010
Country: Brazil	Approval FY: 2010			
Product Line: IBRD/IDA	Region: LATIN AMERICA AND CARIBBEAN	Lending Instrument: Specific Investment Loan		
Implementing Agency(ies):				

**Key Dates**

Board Approval Date	04-May-2010	Original Closing Date	30-Jun-2014	Planned Mid Term Review Date	Last Archived ISR Date	07-Jun-2010
Effectiveness Date	00000000	Revised Closing Date	30-Jun-2014	Actual Mid Term Review Date		

**Project Development Objectives**

Project Development Objective (from Project Appraisal Document)

Has the Project Development Objective been changed since Board Approval of the Project?

Yes     No

**Component(s)**

Component Name	Component Cost
Part A: Infrastructure and Equipment Investment	542.00
Part B: Technical Assistance	34.40

**Overall Ratings**

	Previous Rating	Current Rating
Progress towards achievement of PDO	Moderately Satisfactory	Moderately Satisfactory
Overall Implementation Progress (IP)	Moderately Satisfactory	Moderately Satisfactory
Overall Risk Rating		Low

**Implementation Status Overview**

The Project was approved by the Board and the loan has been signed. Project implementation is progressing but is behind the original schedule from appraisal. Procurement for the main two civil works (L42-01 and L42-02 to finishing of stations built in Phase 1 and the extension to Vila Sonia) is underway but slower than expected. Resettlement/ expropriation in the area of the extension is also underway.

**Results**

Public Disclosure Authorized

Public Disclosure Authorized

Indicator	Baseline	Current	End Target

Indicator	Baseline	Current	End Target

**Data on Financial Performance (as of 04-Oct-2010)**


**Financial Agreement(s) Key Dates**

Project	Loan No.	Status	Approval Date	Signing Date	Effectiveness Date	Closing Date
P106390	IBRD-78690	Not Effective	04-May-2010	27-Sep-2010	00000000	30-Jun-2014

**Disbursements (in Millions)**

	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P106390	IBRD-78690	0.00	0.00	0.00	0.00	0.00	

**Disbursement Graph**

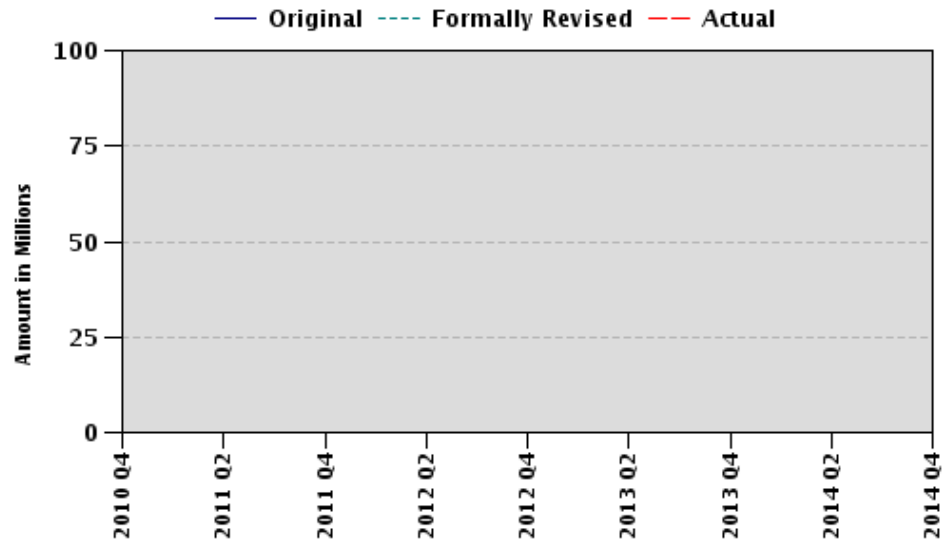

**Key Decisions Regarding Implementation**

The Bank project team will continue to work with Sao Paulo Metro on the pace of implementation and strengthening of environmental and resettlement monitoring systems.

**Restructuring History**

**Related Projects**
