



## Myanmar Flood and Landslide Emergency Recovery Project (P158194)

EAST ASIA AND PACIFIC | Myanmar | Social, Urban, Rural and Resilience Global Practice Global Practice | IBRD/IDA | Investment Project Financing | FY 2017 | Seq No: 6 | ARCHIVED on 14-Jun-2019 | ISR36995 |

Implementing Agencies: Ministry of Agriculture, Livestock, and Irrigation, Republic of the Union of Myanmar, Ministry of Construction, Ministry of Planning and Finance

### Key Dates

#### Key Project Dates

Bank Approval Date: 14-Jul-2016

Effectiveness Date: 20-Feb-2017

Planned Mid Term Review Date: 28-Jan-2019

Actual Mid-Term Review Date: 23-Jan-2019

Original Closing Date: 31-Dec-2021

Revised Closing Date: 31-Dec-2021

### Project Development Objectives

Project Development Objective (from Project Appraisal Document)

To support the recovery in priority areas affected by the 2015 floods and landslides in Myanmar and, in the event of another Eligible Crisis or Emergency, to provide immediate and effective response to said Eligible Crisis or Emergency.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

### Components

Name

Component 1: Resilient Rehabilitation of National Roads:(Cost \$105.00 M)

Component 2: Resilient Rehabilitation of Rural Roads and Livelihoods Support:(Cost \$70.00 M)

Component 3: Provision of Eligible Goods:(Cost \$15.00 M)

Component 4: Project Management and Knowledge Support:(Cost \$10.00 M)

Component 5: Contingent Emergency Response

### Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Moderately Satisfactory	● Moderately Satisfactory
Overall Implementation Progress (IP)	● Moderately Satisfactory	● Moderately Satisfactory
Overall Risk Rating	● High	● High

### Implementation Status and Key Decisions

Progress was made on the first civil works over the past eight months in Rakhine State and the Ayeyarwady Region. To-date 20 km of roads have been rehabilitated, 900 m of resilient structures (retaining walls and box culverts) have been built, and 89,000 workdays have been created. Efforts were made to improve social and environmental safeguards management in Chin State with enhanced environment, health and safety measures for workers and public implemented. Efforts are ongoing to advance the preparation of the next phase of simpler works to be implemented in 2019, and to advance selection of a detailed designs and supervision firm for more complex works. A restructuring is planned to



accommodate institutional changes, extend the project closing date by 23 months, and adjust the results framework. The next implementation support mission is planned for fall of 2019.

## Risks

### Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	● High	● High	● High
Macroeconomic	● Moderate	● Moderate	● Moderate
Sector Strategies and Policies	● Moderate	● Moderate	● Moderate
Technical Design of Project or Program	● Substantial	● Substantial	● Substantial
Institutional Capacity for Implementation and Sustainability	● High	● High	● High
Fiduciary	● High	● High	● High
Environment and Social	● Moderate	● Moderate	● Moderate
Stakeholders	● Substantial	● Substantial	● Substantial
Other	● Substantial	● Substantial	● Substantial
Overall	● Substantial	● High	● High

## Results

### PDO Indicators by Objectives / Outcomes

Support the recovery in priority areas affected by the 2015 floods and landslides in Myanmar				
▶ Direct project beneficiaries (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	59,468.00	1,154,500.00
Date	17-Oct-2016	30-Nov-2018	07-May-2019	31-Dec-2021
▲ Female beneficiaries (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	50.00	50.00
▶ Length of road rehabilitated (rural/non-rural) (Kilometers, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	20.00	20.00	555.00
Date	17-Oct-2016	30-Nov-2018	07-May-2019	31-Dec-2021
<b>►Number of workdays generated (Number, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	29,229.00	89,020.00	865,000.00
Date	17-Oct-2016	30-Nov-2018	07-May-2019	31-Dec-2021
<b>▲Workdays generated by women (Percentage, Custom Supplement)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	12.40	14.00	50.00

**Overall Comments**

The MTR recommended modifications to the original results indicators, in particular the intermediate and target values, based on improved baseline information and current implementation timelines. The proposed changes will be confirmed through the forthcoming project restructuring.

**Intermediate Results Indicators by Components**

<b>Component 1: Resilient Rehabilitation of National Roads</b>				
<b>►Roads rehabilitated, Non-rural (Kilometers, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	155.00
Date	17-Oct-2016	30-Nov-2018	07-May-2019	31-Dec-2021
<b>►Improved disaster and climate resilient designs and standards for national roads developed (Yes/No, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	No	No	Yes
Date	17-Oct-2016	30-Nov-2018	07-May-2019	31-Dec-2021

<b>Component 2: Resilient Rehabilitation of Rural Roads and Livelihoods Support</b>				
<b>►Roads rehabilitated, Rural (Kilometers, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	20.00	20.00	400.00
Date	17-Oct-2016	30-Nov-2018	07-May-2019	31-Dec-2021
<b>►Length of road maintained (rural) (Kilometers, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	300.00
Date	17-Oct-2016	30-Nov-2018	30-Nov-2018	31-Dec-2021

<b>Component 3: Provision of Eligible Goods</b>				
<b>►Goods procured and distributed as outlined in the CERIP (Percentage, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	100.00	100.00	100.00
Date	01-Sep-2016	28-Sep-2018	07-May-2019	31-Dec-2021

<b>Component 4: Project Management and Knowledge Support</b>				
<b>►Grievances registered related to delivery of project benefits addressed (%) (Percentage, Custom)</b>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	100.00	89.00	95.00
Date	17-Oct-2016	30-Nov-2018	07-May-2019	31-Dec-2021

**Overall Comments**

Length of road maintained: Maintenance will be conducted only on the roads that are rehabilitated under the project. The first roads were finalized in April 2019 and basic maintenance will start only next year on these finalized rural roads. In the meanwhile, draft community-based maintenance guidelines were developed under the project to guide maintenance. They not only support road maintenance but livelihoods and create jobs through the use of labor-intensive works, where appropriate. Community-based approaches to routine maintenance have been successfully implemented in other countries, such as Vietnam and Laos. These programs allow women to be actively involved in routine maintenance activities, develop skills, and earn an income.

Grievances registered and addressed: The slight drop from the last ISR is caused by the fact that the project only recently started to receive and monitor grievances after the start of civil works, and only now accurate numbers available. Most of the grievances received are suggestions to change the design of the road and engineering aspects. In any functioning grievance system, at any point in time, there will be grievances that are not yet resolved but are being worked on. This is the case with the project - the PMU is now reporting accurately about grievances received, grievances resolved and grievances that they are working on resolving



with details on how they plan to proceed. The change in the numbers demonstrates the PMU has improved in registering, resolving and reporting on grievances.

### Data on Financial Performance


#### Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P158194	IDA-58890	Effective	USD	200.00	200.00	0.00	21.66	175.98	11%

#### Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P158194	IDA-58890	Effective	14-Jul-2016	25-Nov-2016	20-Feb-2017	31-Dec-2021	31-Dec-2021

#### Cumulative Disbursements

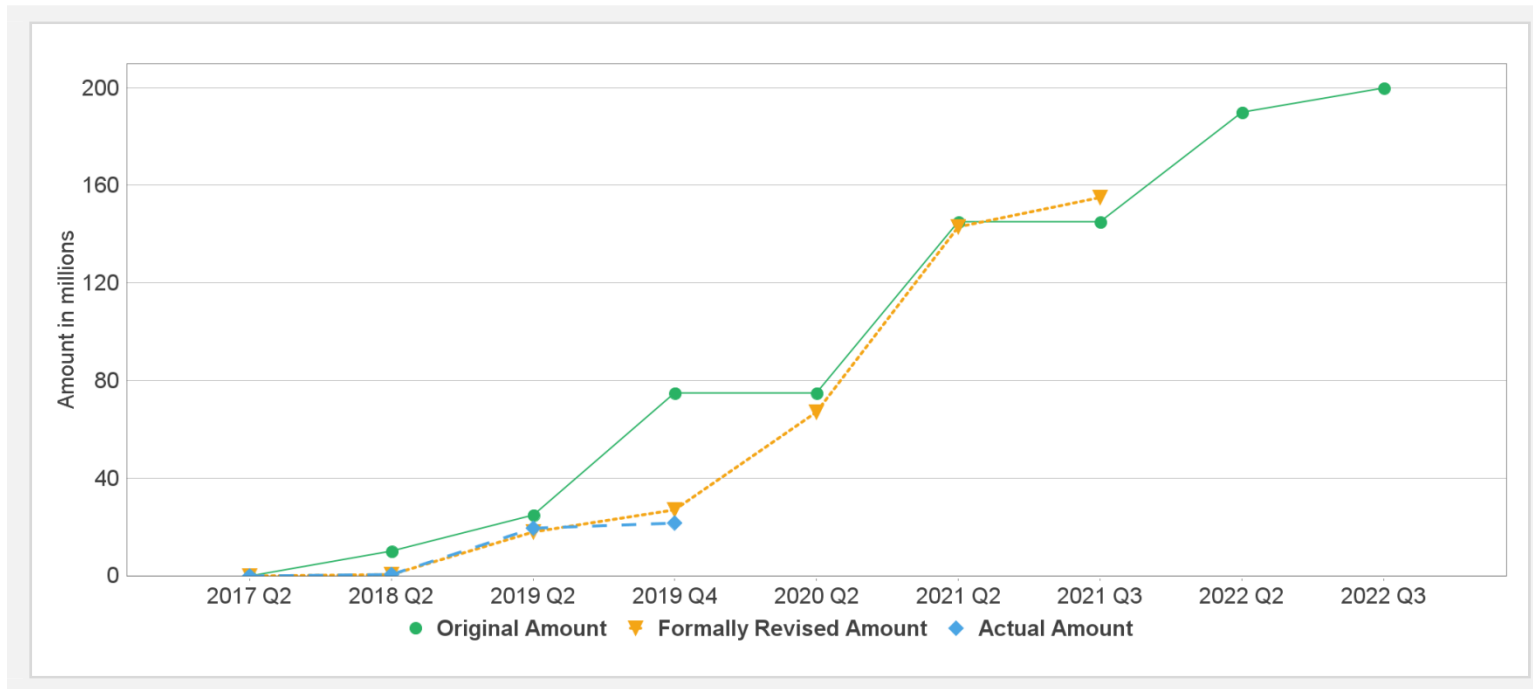



### **Restructuring History**

There has been no restructuring to date.

### **Related Project(s)**

There are no related projects.

---
