



Public Disclosure Authorized

Preparation of a Program Towards Sustainable Flood Management in the Greater Metro Manila Area Project (P145237)

EAST ASIA AND PACIFIC | Philippines | Water Global Practice | Recipient Executed Activities | Investment Project Financing | FY 2015 | Seq No: 7 | ARCHIVED on 08-Aug-2019 | ISR38185 |

Implementing Agencies: Department of Public Works and Highways, Department of Finance

Key Dates

Key Project Dates

Bank Approval Date: 16-Sep-2014

Effectiveness Date: 19-Jun-2015

Original Closing Date: 31-Jan-2017

Revised Closing Date: 31-Jan-2020

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The objective is to prepare priority projects, identified by the flood management master plan, that aim to improve flood management and resilience in and around Metro Manila.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Public Disclosure Authorized

Components

Name

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Moderately Satisfactory	● Moderately Satisfactory
Overall Implementation Progress (IP)	● Moderately Satisfactory	● Moderately Satisfactory

Implementation Status and Key Decisions

Technical consultant have been recruited to prepare a feasibility study and subsequently the design of the selected option for flood management improvement in the Pasig-Marikina River Basin. Alternatives have been analyzed and a feasibility study was prepared as per terms of reference. Based on the review of the study report and technical discussions a preferred solution was selected. The design of this solution will be

prepared during the next six months. Environmental and social consultants have been recruited to prepare the environmental and social impact assessment.

Risks

Overall Risk Rating

Risk Category	Rating at Approval	Previous Rating	Current Rating
Overall	--	● Moderate	● Moderate

Results

Project Development Objective Indicators

►Proposals for Upper Marikina River structural measures fully designed that are technically, economically, socially, and environmentally sound and that are ready for appraisal. (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1.00
Date	22-Dec-2014	01-Feb-2019	31-Jul-2019	31-Jan-2020

►Proposals for an integrated flood forecasting and early warning system fully designed and ready for appraisal. (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1.00
Date	22-Dec-2014	01-Feb-2019	31-Jul-2019	31-Jan-2020

►Proposals for institutional arrangements for sustainable flood management in the Greater Metro Manila Area acceptable to the Government of the Philippines and key stakeholders and ready for implementa (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1.00
Date	22-Dec-2014	01-Feb-2019	31-Jul-2019	31-Jan-2020

Overall Comments

Intermediate Results Indicators

► Feasibility study for the proposed interventions in Upper Marikina River completed. (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	1.00	1.00
Date	22-Dec-2014	01-Feb-2019	31-May-2019	10-Apr-2019

► Mid-term report with draft proposals for institutional arrangements for sustainable flood management completed. (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	1.00
Date	22-Dec-2014	01-Feb-2019	31-Jul-2019	30-Nov-2019

Overall Comments

Data on Financial Performance**Disbursements (by loan)**




Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P145237	TF-18611	Effective	USD	2.73	2.73	0.00	0.30	2.43	11%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P145237	TF-18611	Effective	04-Jun-2015	19-Jun-2015	19-Jun-2015	31-Jan-2017	31-Jan-2020

Cumulative Disbursements

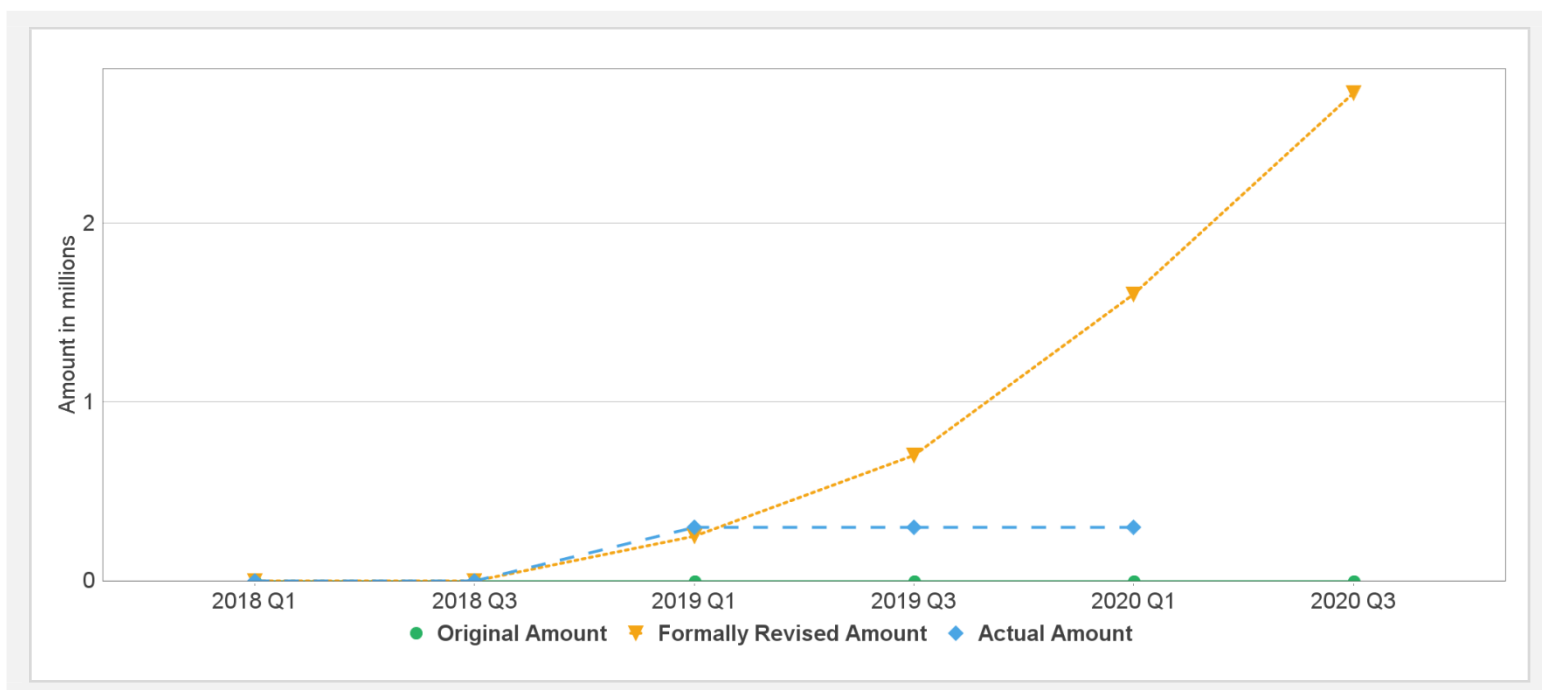

Restructuring History

Level 2 Approved on 24-Jan-2017 ,Level 2 Approved on 30-Jan-2018

Related Project(s)

There are no related projects.
