



AFCC2/RI-Great Lakes Trade Facilitation (P151083)

AFRICA | Africa | Macroeconomics, Trade and Investment Global Practice |
IBRD/IDA | Investment Project Financing | FY 2016 | Seq No: 7 | ARCHIVED on 05-Feb-2019 | ISR35130 |

Implementing Agencies: Rwanda Ministry of Industry and Trade, COMESA, DRC Ministry of Finance, Government of Rwanda, Uganda Minister of Finance, Planning and Economic Development, Rwanda Civil Aviation Authority (RCAA), Rwanda Local Development Agency (LODA), Rwanda Transport Development Agency (RTDA), DRC Cellule Infrastructure of MITPR (CI/MITPR), DRC Ministry of Commerce (SG/MC), Uganda Ministry of Trade, Industry & Cooperatives (MTIC)

Key Dates

Key Project Dates

Bank Approval Date: 25-Sep-2015	Effectiveness Date: 25-Jan-2016
Planned Mid Term Review Date: 02-Mar-2020	Actual Mid-Term Review Date: 19-Dec-2018
Original Closing Date: 31-Dec-2020	Revised Closing Date: 31-Dec-2020

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The Development Objective of this project is to facilitate cross-border trade by increasing the capacity for commerce and reducing the costs faced by traders, especially small-scale and women traders, at targeted locations in the borderlands.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Component 1: Improving core trade infrastructure and facilities in the border areas:(Cost \$54.35 M)
Component 2: Implementation of Policy and Procedural Reforms and Capacity Building to Facilitate Cross Border Trade in Goods and Services:(Cost \$9.50 M)
Component 3: Performance Based Management in Cross Border Administration:(Cost \$4.55 M)
Component 4: Implementation support, Communication and M&E:(Cost \$10.60 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Moderately Unsatisfactory	● Moderately Unsatisfactory
Overall Implementation Progress (IP)	● Moderately Unsatisfactory	● Moderately Unsatisfactory
Overall Risk Rating	● High	● High

Implementation Status and Key Decisions

During the reporting period, progress was made in the implementation of project activities, including opening of temporary physical infrastructure at two project sites in the DRC and interventions related to training, capacity building and policy reform. There is a marked difference in the organized flow of traders, greater efficiency in the use of the jeton system by small-scale cross-border traders, and the use of the trade information desks officers (TIDOS). Most notably, the DRC successfully implemented new temporary infrastructure at Ruzizi 1 and the Petite Barriere. In



Rwanda, contracts were signed for the construction of the Nyamasheke cross-border market, the feasibility study for Kamonyola cross-border market, the design review for Rsuizi 1 OSBP, and contracts for packages 1,2,3 and 4 for Kamemebe airport should be signed before February 2019. In Uganda, the project team has made progress in all 4 project components and will focus on reducing procurement delays for the works contracts for the Mpondwe and Bunugana cross-border infrastructure and the Mpondwe border market. COMESA has made significant progress with the use of Trade Information Desk officers in resolving conflicts for traders, in developing the communications strategy, implementing the Training of the Trainers program and in awareness building of the STR. However, despite these important outcomes, disbursement remains significantly behind schedule. This is mainly due to continuing delays in procurement processes. The team, therefore, recommends an implementation progress rating of **Moderately Unsatisfactory (MU)** and DO rating of **Moderately Unsatisfactory (MU)**. The team believes that in each of the project counterparts, many of the procurement obstacles are being addressed so as to allow significant progress in the coming period and that implementation of the contracts recently signed and those expected to be signed shortly will lead to a significant increase in project disbursements.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	● High	● High	● High
Macroeconomic	● Substantial	● Substantial	● Substantial
Sector Strategies and Policies	● High	● Substantial	● Substantial
Technical Design of Project or Program	● Substantial	● Substantial	● Substantial
Institutional Capacity for Implementation and Sustainability	● Substantial	● Substantial	● Substantial
Fiduciary	● High	● High	● High
Environment and Social	● Substantial	● Substantial	● Substantial
Stakeholders	● High	● High	● High
Other	--	--	--
Overall	● High	● High	● High

Results

PDO Indicators by Objectives / Outcomes

Reduced costs for traders, especially small-scale and women traders at targeted locations				
▶ Average time for traders to cross target border crossings (Minutes, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	18.00	--	14.65	5.00
Date	16-Apr-2015	--	20-Dec-2018	21-Dec-2020
▶ Incidence of harassment of small scale traders (Percentage, Custom)				



	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	92.00	--	32.70	10.00
Date	25-Jun-2015	--	20-Dec-2018	21-Dec-2020
▲-- Among female traders (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	96.00	--	52.10	10.00
Date	25-Jun-2015	--	20-Dec-2018	21-Dec-2020
▲Kasindi (DRC) - Mpondwe (Ug) (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	65.00	--	26.00	10.00
Date	06-Apr-2015	--	20-Dec-2018	21-Dec-2020
▲Rusizi 1 (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	85.00	--	29.00	10.00
Date	06-Apr-2015	--	20-Dec-2018	21-Dec-2020
▲Petite Barriere (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	96.00	--	43.00	10.00
Date	06-Apr-2015	--	20-Dec-2018	21-Dec-2020
▶Value of goods handled through core trade infrastructure (Amount(USD), Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	92.00	--	333.00	117.00
Date	06-Apr-2015	--	20-Dec-2018	21-Dec-2020
▲DRC - Rwanda (Amount(USD), Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	92.00	--	88.06	117.00
Date	06-Apr-2015	--	20-Dec-2018	21-Dec-2020
▲DRC - Uganda (Amount(USD), Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	110.00	--	244.94	140.00



Date	06-Apr-2015	--	20-Dec-2018	21-Dec-2020
►Direct project beneficiaries (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	77,428.00	40,000.00
Date	06-Apr-2015	--	20-Dec-2018	21-Dec-2020
▲Uganda (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	3,317.00	20,000.00
Date	06-Apr-2015	--	20-Dec-2018	21-Dec-2020
▲Rwanda (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	35,792.00	20,000.00
Date	06-Apr-2015	--	20-Dec-2018	21-Dec-2020
▲DRC (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	38,319.00	40,000.00
Date	06-Apr-2015	--	20-Dec-2018	21-Dec-2020
▲Female beneficiaries (Percentage, Custom Supplement)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	75.00	65.00
▲Uganda (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	75.00	65.00
Date	06-Apr-2015	--	20-Dec-2018	21-Dec-2020
▲Rwanda (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	80.00	65.00
Date	06-Apr-2015	--	20-Dec-2018	21-Dec-2020
▲DRC (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	0.00	--	75.00	65.00
Date	06-Apr-2015	--	20-Dec-2018	21-Dec-2020

Intermediate Results Indicators by Components

Component 2: Implementation of Policy and Procedural Reforms and Capacity Building to Facilitate Cross Border Trade in Goods and Services				
▶ Daily average number of traders processed through the borders (entry and exit) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	150.00	--	46,542.00	250.00
Date	25-Jun-2015	--	21-Dec-2018	30-Sep-2019
▲ Rusizi (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	1,000.00	--	18,721.00	1,300.00
Date	25-Jun-2015	--	20-Dec-2018	30-Sep-2019
▲ Petite Barriere (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	2,500.00	--	20,793.00	3,500.00
Date	25-Jun-2015	--	20-Dec-2018	30-Sep-2019
▲ Bunagana (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	150.00	--	2,238.00	250.00
Date	25-Jun-2015	--	21-Dec-2018	30-Sep-2019
▲ Kasindi/Mpondwe (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	600.00	--	3,305.00	700.00
Date	25-Jun-2015	--	21-Dec-2018	30-Sep-2019
▲ Mahagi/Goli (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	150.00	--	1,485.00	250.00



Date	25-Jun-2015	--	21-Dec-2018	30-Sep-2019
▶Number of regional workshps/seminars held for peer-to-peer learning, sharing best practices on ICBT monitoring _ COMESA (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	2.00	3.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▶# of Border Officials receiving training (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	269.00	1,200.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Uganda (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	29.00	360.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Rwanda (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	60.00	240.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲DRC (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	180.00	600.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▶Number of facilitators trained on the delivery of training to traders and border officials (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	195.00	60.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲DRC (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	69.00	20.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020



▲Rwanda (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	65.00	20.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Uganda (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	61.00	20.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▶Incidence of bribery/solicitation of informal payments from traders. (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	45.00	--	27.70	10.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Kasindi (DRC) – Mpondwe (Ug) (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	54.00	--	21.10	10.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Rusizi 1 (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	78.00	--	28.20	10.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Petite Barrière (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	93.00	--	33.70	10.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▶Incidence of physical and/or verbal harassment of traders. (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	28.00	--	21.90	10.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Kasindi (DRC) – Mpondwe (Ug) (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target



Value	8.90	--	8.50	5.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Rusizi 1 (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	37.00	--	14.80	10.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Petite Barrière (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	28.00	--	28.00	10.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▶# of Traders receiving training (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	865.00	4,000.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲DRC (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	2,000.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Rwanda (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	200.00	800.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Uganda (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	665.00	1,200.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020

Component 1: Improving core trade infrastructure and facilities in the border areas

▶Degree of completion of airport improvement works _ Rwanda (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
--	----------	-------------------	------------------	------------



Value	10.00	--	20.00	100.00
Date	06-Apr-2015	--	20-Dec-2018	21-Dec-2020
►Completion of planned feasibility studies (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	2.00	12.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲DRC (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	7.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Rwanda (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	2.00	3.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Uganda (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	2.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
►Number of passengers flying through Kamembe airport _ Rwanda (Number (Thousand), Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	43.30	--	19.70	92.80
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
►Completed physical improvements to border facilities (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	7.00
Date	25-Jun-2015	--	21-Dec-2018	21-Dec-2020
▲Uganda (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	1.00



Date	06-Apr-2015	--	21-Dec-2018	30-Sep-2019
▲Rwanda (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	1.00
Date	06-Apr-2015	--	21-Dec-2018	30-Sep-2019
▲DRC (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	3.00
Date	06-Apr-2015	--	21-Dec-2018	30-Sep-2019
▶Construction of border markets (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	4.00
Date	06-Apr-2015	--	20-Dec-2018	21-Dec-2020
▶Value of goods exchanged in new border markets. (Amount(USD), Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	300.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Uganda (Amount(USD), Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	300.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Rwanda (Amount(USD), Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	495.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲DRC (Amount(USD), Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	350.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020



▶Number of market users (monthly average) (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	1,200.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Uganda (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	1,200.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Rwanda (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	1,200.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲DRC (Number, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	1,500.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020

Component 3: Performance Based Management in Cross Border Administration				
▶Improved perception of traders regarding the quality of services provided by border agencies (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	59.00	10.00
Date	06-Apr-2015	--	20-Dec-2018	21-Dec-2020
▲Petite Barrière (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	52.00	10.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Rusizi 1 (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	69.00	10.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020



▲Kasindi (DRC) – Mpondwe (Ug) (Percentage, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	57.00	10.00
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▶Functional review completed at the Customs and Immigration offices (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	--	No	Yes
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲DRC (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	--	No	Yes
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Rwanda (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	--	No	Yes
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Uganda (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	--	No	Yes
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020

Component 4: Implementation support, Communication and M&E				
▶Development and execution of project communications strategy. (Yes/No, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	--	Yes	Yes
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
▲Uganda (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	--	Yes	Yes
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020



DRC (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	--	Yes	Yes
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
Rwanda (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	--	Yes	Yes
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020
COMESA (Yes/No, Custom Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No	--	No	Yes
Date	06-Apr-2015	--	21-Dec-2018	21-Dec-2020

Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P151083	IDA-57210	Effective	USD	26.00	26.00	0.00	6.48	19.63	25%
P151083	IDA-57220	Effective	USD	14.00	14.00	0.00	1.86	12.23	13%
P151083	IDA-57240	Effective	USD	34.00	34.00	0.00	6.79	27.16	20%
P151083	IDA-D0890	Effective	USD	5.00	5.00	0.00	2.79	2.25	55%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P151083	IDA-57210	Effective	25-Sep-2015	26-Oct-2015	25-Jan-2016	31-Dec-2020	31-Dec-2020
P151083	IDA-57220	Effective	25-Sep-2015	23-Mar-2017	17-Apr-2017	31-Dec-2020	31-Dec-2020
P151083	IDA-57240	Effective	25-Sep-2015	27-Oct-2015	15-Sep-2016	31-Dec-2020	31-Dec-2020
P151083	IDA-D0890	Effective	25-Sep-2015	19-Nov-2015	04-Apr-2016	31-Dec-2020	31-Dec-2020

Cumulative Disbursements

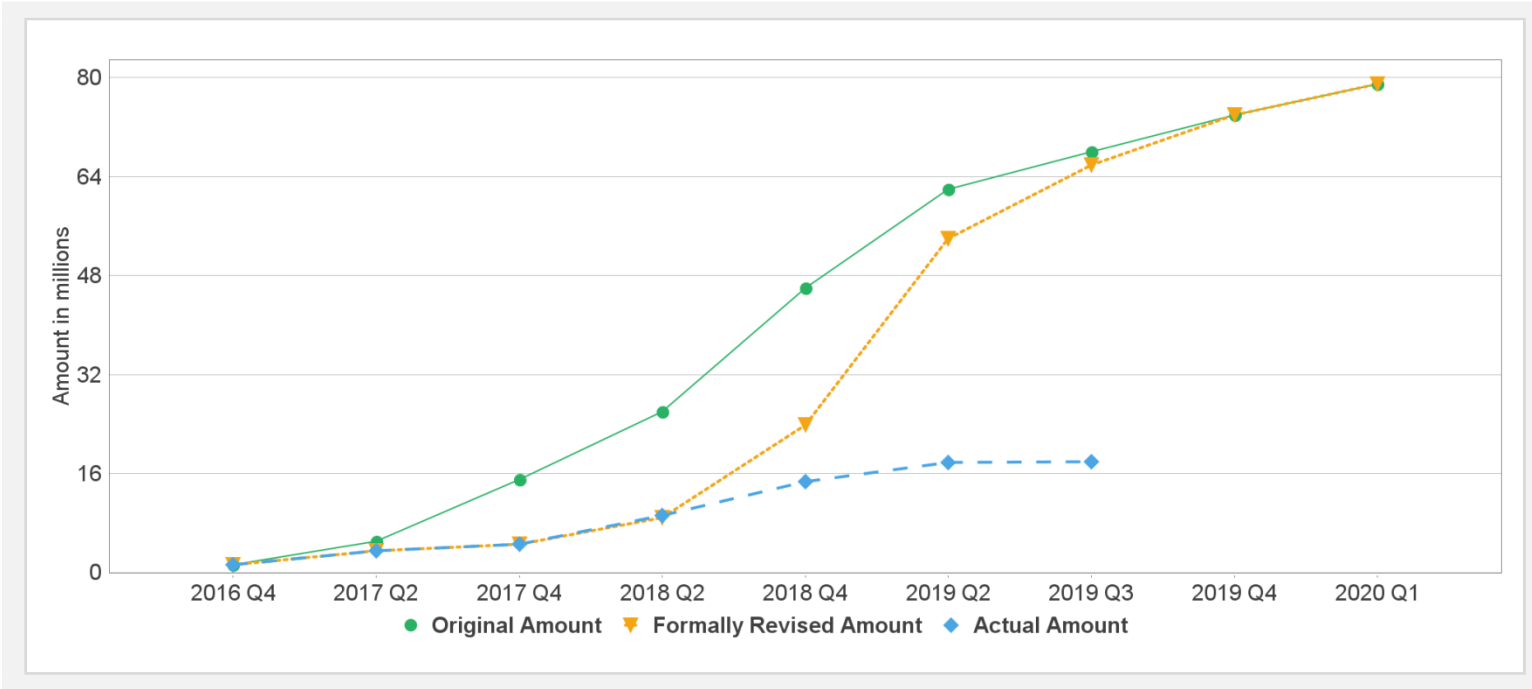

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
