

**CI: Cote d'Ivoire E-Agriculture Project (P160418)**

AFRICA | Cote d'Ivoire | Transport & Digital Development Global Practice |
IBRD/IDA | Investment Project Financing | FY 2018 | Seq No: 1 | ARCHIVED on 13-Nov-2018 | ISR33909 |

Implementing Agencies: Ministry of Digital Economy and Post, Republic of Cote d'Ivoire

Key Dates**Key Project Dates**

Bank Approval Date: 25-May-2018

Effectiveness Date: --

Planned Mid Term Review Date: --

Actual Mid-Term Review Date: --

Original Closing Date: 30-Jun-2023

Revised Closing Date: 30-Jun-2023

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The Project Development Objective is to increase access to digital services and leverage digital platforms to improve farm productivity and access to markets.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Extending digital connectivity in rural and remote areas:(Cost \$31.50 M)
Digital services for sustainable agricultural development:(Cost \$12.50 M)
Rehabilitation and maintenance of rural access roads:(Cost \$19.50 M)
Program implementation and monitoring:(Cost \$6.50 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	--	● Satisfactory
Overall Implementation Progress (IP)	--	● Satisfactory
Overall Risk Rating	--	● Substantial

Implementation Status and Key Decisions

The execution of the Project Preparation Advance is Satisfactory with a 90% disbursement rate, ahead of credit effectiveness (expected by end of November). The launch of Component 3 (Rehabilitation of Rural Access Roads) mid November will certainly boost disbursement. The Project Implementation Unit must now focus on the involvement and partnerships with private investors, in particular mobile operators, to plan the broadband coverage of all targeted zones in the country.



Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	● Substantial	--	● Substantial
Macroeconomic	● Substantial	--	● Substantial
Sector Strategies and Policies	● Moderate	--	● Moderate
Technical Design of Project or Program	● Substantial	--	● Substantial
Institutional Capacity for Implementation and Sustainability	● Substantial	--	● Substantial
Fiduciary	● Moderate	--	● Moderate
Environment and Social	● Substantial	--	● Substantial
Stakeholders	● Moderate	--	● Moderate
Other	--	--	--
Overall	● Substantial	--	● Substantial

Results

PDO Indicators by Objectives / Outcomes

Increase access to digital services in rural areas				
▶ People provided with access to the Internet (Number, Corporate)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	5,000,000.00	--	0.00	6,000,000.00
Date	28-Feb-2018	--	07-Nov-2018	30-Jun-2023
▲ Number of people that benefitted from new access to Internet service. (Number, Corporate Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	1,000,000.00
Date	28-Feb-2018	--	07-Nov-2018	30-Jun-2023
▲ Number of people that benefitted from the improved Internet service. (Number, Corporate Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	1,000,000.00
Date	28-Feb-2018	--	07-Nov-2018	30-Jun-2023



▲People provided with access to the Internet - Female (Number, Corporate Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	400,000.00	--	400,000.00	500,000.00
Date	28-Feb-2018	--	07-Nov-2018	30-Jun-2023

Leverage digital platforms to improve farm productivity and access to markets

▶Farmers reached with agricultural assets or services (Number, Corporate)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	1,000,000.00
Date	28-Feb-2018	--	07-Nov-2018	30-Jun-2023

▲Farmers reached with agricultural assets or services - Female (Number, Corporate Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	700,000.00
Date	28-Feb-2018	--	07-Nov-2018	30-Jun-2023

▶Beneficiaries that feel project investments reflected their needs (%) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	80.00
Date	28-Feb-2018	--	07-Nov-2018	30-Jun-2023

▶Percentage increase in revenues of the targeted beneficiaires (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	10.00
Date	28-Feb-2018	--	07-Nov-2018	30-Jun-2023

Intermediate Results Indicators by Components

Component 2 - Digital services for sustainable agricultural development				
▶Beneficiaries of job-focused interventions (Number, Corporate)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	10,000.00



Date	28-Feb-2018	--	07-Nov-2018	30-Jun-2023
▲Beneficiaries of job-focused interventions - Female (Number, Corporate Breakdown)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	7,000.00
Date	28-Feb-2018	--	07-Nov-2018	30-Jun-2023
▶Share of women within the newly established cooperatives/producers organizations (led by women) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	90.00
Date	29-Jun-2018	--	07-Nov-2018	30-Jun-2023
▶Increase in share of women in leadership roles (among the targeted beneficiaries) (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	20.00
Date	29-Jun-2018	--	07-Nov-2018	30-Jun-2023

Component 3 - Rehabilitation and maintenance of rural access roads to access production areas

▶Roads rehabilitated (Kilometers, Corporate)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	2,800.00
Date	29-Jun-2018	--	07-Nov-2018	30-Jun-2023

▲Roads rehabilitated - rural (Kilometers, Corporate Breakdown)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	2,800.00
Date	29-Jun-2018	--	07-Nov-2018	30-Jun-2023

Data on Financial Performance

Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
---------	----------------	--------	----------	----------	---------	-----------	-----------	-------------	-------------




P160418	IDA-62440	Not Effective	USD	70.00	70.00	0.00	0.00	66.81		0%
---------	-----------	---------------	-----	-------	-------	------	------	-------	--	----

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P160418	IDA-62440	Not Effective	25-May-2018	21-Jun-2018	--	30-Jun-2023	30-Jun-2023

Cumulative Disbursements

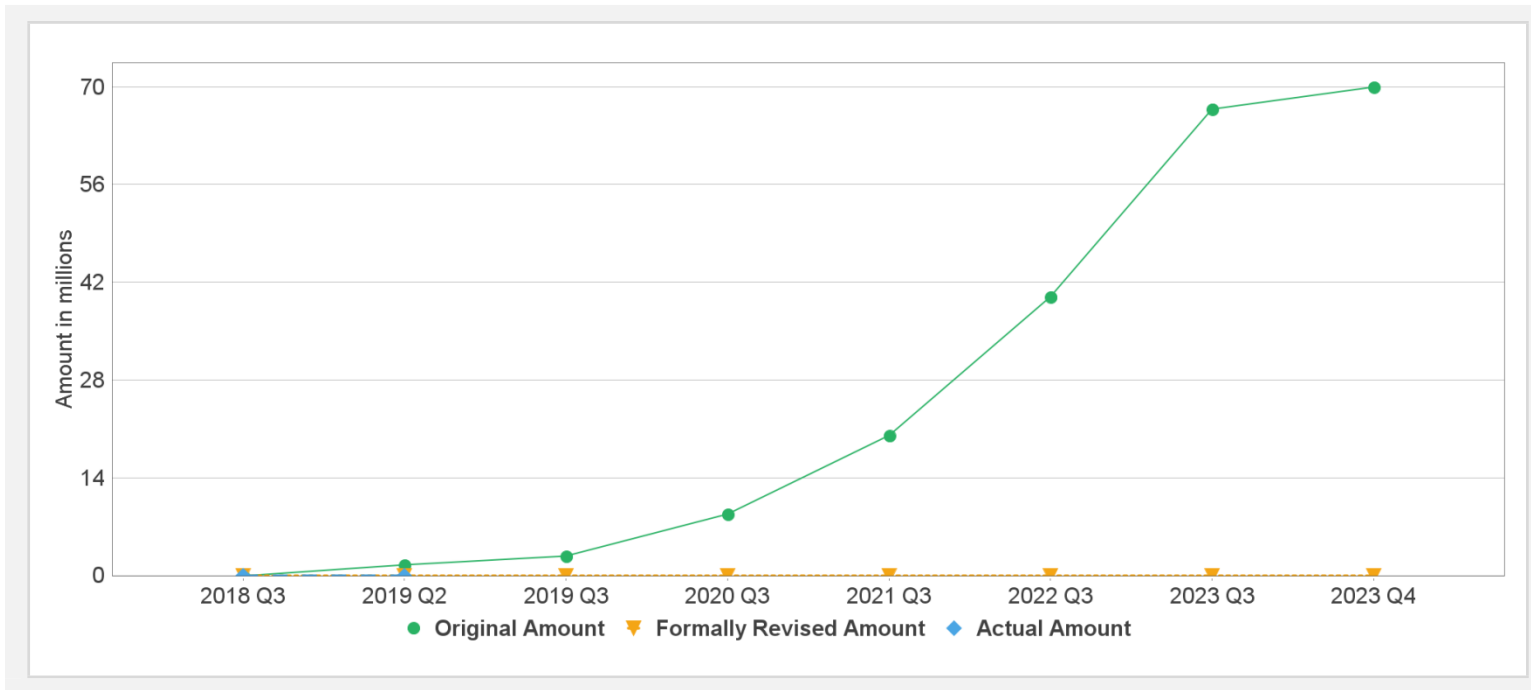

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
