



Jordan Ozone Depleting Substances HCFC Phase-Out Project (ODS3) (P127702)

MIDDLE EAST AND NORTH AFRICA | Jordan | Environment & Natural Resources Global Practice | Montreal Protocol | Investment Project Financing | FY 2013 | Seq No: 13 | ARCHIVED on 31-May-2019 | ISR37270 |

Implementing Agencies: Hashemite Kingdom of Jordan, Ministry of Environment

Key Dates

Key Project Dates

Bank Approval Date: 26-Apr-2013

Effectiveness Date: 19-May-2013

Planned Mid Term Review Date: 26-Feb-2016

Actual Mid-Term Review Date: 14-Feb-2016

Original Closing Date: 31-Dec-2022

Revised Closing Date: 31-Dec-2022

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The project development objective is to support Jordan in its overall efforts to meet its first Montreal Protocol HCFC phase-out obligations between 2013 and 2017, and to strengthen the capacity of responsible government entities to continue to effectively implement the Montreal Protocol.

Has the Project Development Objective been changed since Board Approval of the Project Objective?

Yes

Board Approved Revised Global Environmental Objective (If project is formally restructured)

The project development objective is to support Jordan in its overall efforts to meet its Montreal Protocol HCFC phase-out obligations, and to strengthen the capacity of responsible government entities to continue to effectively implement and comply with the Montreal Protocol.

Components

Name

Technical Assistance, Policy and Sector Plan Management:(Cost \$0.81 M)

Investment in HCFC Consumption Reductions:(Cost \$2.24 M)

Institutional Strengthening:(Cost \$0.86 M)

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	● Satisfactory	● Satisfactory
Overall Implementation Progress (IP)	● Moderately Unsatisfactory	● Moderately Unsatisfactory
Overall Risk Rating	● Substantial	● Substantial

Implementation Status and Key Decisions

Project management has significantly improved, with the Secretary General of the MOE also serving as the head of the National Ozone Unit and providing personal leadership to the PMU. Staffing has strengthened with experienced technical officer being hired to assist with the processing of the sub-project agreements.

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	● Moderate	● Moderate



Macroeconomic	--	● Substantial	● Substantial
Sector Strategies and Policies	--	● Low	● Low
Technical Design of Project or Program	--	● Moderate	● Moderate
Institutional Capacity for Implementation and Sustainability	--	● Substantial	● Substantial
Fiduciary	--	● Substantial	● Substantial
Environment and Social	--	● Moderate	● Moderate
Stakeholders	--	● Moderate	● Moderate
Other	--	● High	● High
Overall	--	● Substantial	● Substantial

Results

PDO Indicators by Objectives / Outcomes

To support Jordan in its overall efforts to meet its first MP phaseout obligations				
▶ HCFC consumption within Maximum Allowable Limits (Tones/year, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	83.00	33.55	11.15	41.50
Date	15-Feb-2013	09-Oct-2018	30-Mar-2019	30-Dec-2022
Comments:	Unit of measure: ODP tons or tones of ozone depleting potential 11.15 ODP tons as of Mar 2019 is the preliminary reported HCFC consumption in Jordan.			
▶ Compliance with annual MP and MLF obligations on controlled substances and data reporting (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	100.00	50.00	100.00
Date	15-Feb-2013	09-Oct-2018	30-Apr-2019	30-Dec-2022
Comments:	This indicator measures issuance of licenses and annual quotas fully executed and Article 7 reports submitted by the Montreal Protocol Ozone Secretariat and country program updates submitted by the May deadline to the MLF Secretariat. Annual target comprises 1) timely issuance of licenses of controlled substances; 2) timely issuance of quotas or submission of Article 7 data to the Ozone Secretariat by September 30th and, 4) submission of country program data to the MLF Secretariat by 1st. Each component of the target counts for 25% of 100% compliance. For the 2017 reporting year, all 4 of these parameters have been achieved			
▶ Avoided emission of tons of CO2 equivalent from transition to new technology in the AC and foam sectors (Tones/year, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	60,095.00	60,095.00	313,620.00



Date	15-Feb-2013	09-Oct-2018	30-Apr-2019	30-Dec-2022
Comments:	<p>This indicator measures the level of emissions avoided using the equivalent amount of CO₂ of HCFCs consumed in the AC and foam sectors at baseline, as well as EE improvement.</p> <p>Break down Indicator on AC Sector: This indicator measures avoided emission of tons of CO₂ equivalent from transition to new technology in the AC sector: Level of emissions avoided using the equivalent amount of CO₂ from 80% change of R-410A (compared to R-22) and conservative EE improvement to 2.8 EER.</p> <p>Break down Indicator on Foam Sector: This indicator measures avoided emission of tons of CO₂ equivalent from transition to new technology in the foam sector: Level of emissions avoided using the equivalent amount of CO₂ of HCFC-141b eliminated (including that contained in pre-blended polyol).</p>			
<p>▲Avoided emission of tons of CO₂ equivalent from transition to new technology in the AC sector (Tones/year, Custom Breakdown)</p>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	60,095.00	60,095.00	60,095.00
Date	15-Feb-2013	09-Oct-2018	30-Apr-2019	29-Dec-2017
<p>▲Avoided emission of tons of CO₂ equivalent from transition to new technology in the foam sector (Tones/year, Custom Breakdown)</p>				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	253,525.00
Date	15-Feb-2013	09-Oct-2018	30-Apr-2019	30-Dec-2022

Intermediate Results Indicators by Components

Technical Assistance, Policy and AC Sector Plan Management				
▶Implementation of key policies and regulations for HCFC-141b phase-out (Text, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	No HCFC-141b policy	No HCFC-141b policy	No HCFC-141b policy	Ban on import and use of HCFC-141b and HCFC-141b pre-blended polyol in foam manufacturing
Date	15-Feb-2013	28-Mar-2018	28-Mar-2018	03-Jan-2022
▶Implementation of key policies and regulations for HCFC-22 phase-out (Text, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	no HCFC-22 policy	Ban on use of HCFC-22 policy in manufacturing AC and ban on imports of HCFC-22 based AC units	Ban on use of HCFC-22 policy in manufacturing AC and ban on imports of HCFC-22 based AC units	Ban on use of HCFC-22 policy in manufacturing AC and ban on imports of HCFC-22 based AC units
Date	31-Jan-2013	28-Mar-2018	28-Mar-2018	29-Nov-2019
Comments:	Achieved on 31 December 2016.			



►Satisfactory technical assistance activities delivered (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	8.00	14.00
Date	15-Feb-2013	28-Mar-2018	30-Apr-2018	30-Dec-2022
Comments:	Satisfactory technical assistance activities delivered to strengthen technical capacity of manufacturers to convert from HCFC use and Government officials to monitor and enforce HCFC controls. Two study tours organized for large foam manufacturers to visit foam manufacturers, system houses, and equipment suppliers in Egypt and Dubai.			
►Compliance with MLF HCFC project reporting requirements (Percentage, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	50.00	0.00	100.00
Date	26-Apr-2013	28-Mar-2018	30-Apr-2018	30-Dec-2022
Comments:	Target comprises: 1) annual consumption verification; and 2) preparation and submission to the MLF of implementation progress report and plan. Each component of the target counts for 50% of target. As (2) is only due twice during the project period, the target is not 100% annually. 2 reports (verification and implementation progress report) not due until September 2018.			
Investment in HCFC Consumption Reductions				
►Number of subproject agreement contracts signed with AC manufacturers (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	2.00	2.00	2.00
Date	15-Feb-2013	28-Mar-2018	28-Mar-2018	30-Dec-2022
►Cumulative HCFC-22 consumption phased out in the AC sector (Tones/year, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	1.43	1.43	1.43
Date	15-Feb-2013	28-Mar-2018	28-Mar-2018	28-Dec-2018
Comments:	Unit of Measure: ODP tons or tons of ozone depleting potential			
►Number of foam enterprises participating in subprojects (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	71.00	60.00
Date	15-Feb-2013	28-Mar-2018	30-Apr-2019	30-Dec-2022
►Cumulative HCFC-141b consumption phased out in foam sector (Tones/year, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	0.00	0.00	29.78
Date	15-Feb-2013	28-Mar-2018	30-Apr-2019	30-Dec-2022



Comments:	Unit of measure: ODP tons or tons of ozone depleting potential			
Institutional Strengthening				
▶Number of MP related meetings and workshops attended by NOU (Number, Custom)				
	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	3.00	3.00	3.00
Date	15-Feb-2013	28-Mar-2018	28-Mar-2018	30-Dec-2022
Comments:	Frequency: Annual Attendance of NOU staff at MP Meetings and its Open-ended Working Group (twice annually) and UNEP Ozone Officer Network meetings (at least once annually) will ensure that NOU and MoE staff are current on decisions and policies that relate to MP compliance and that they are aware of the technical developments across MP sectors that impact industry, decision and policy making and enforcement.			

Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P127702	TF-13968	Effective	USD	2.82	1.46	1.36	1.42	0.04	97%
P127702	TF-A5173	Effective	USD	2.45	2.45	0.00	0.00	2.45	0%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P127702	TF-13968	Effective	19-May-2013	19-May-2013	19-May-2013	30-Jun-2019	31-Dec-2022
P127702	TF-A5173	Effective	31-Dec-2017	31-Dec-2017	22-Mar-2018	31-Dec-2022	31-Dec-2022

Cumulative Disbursements

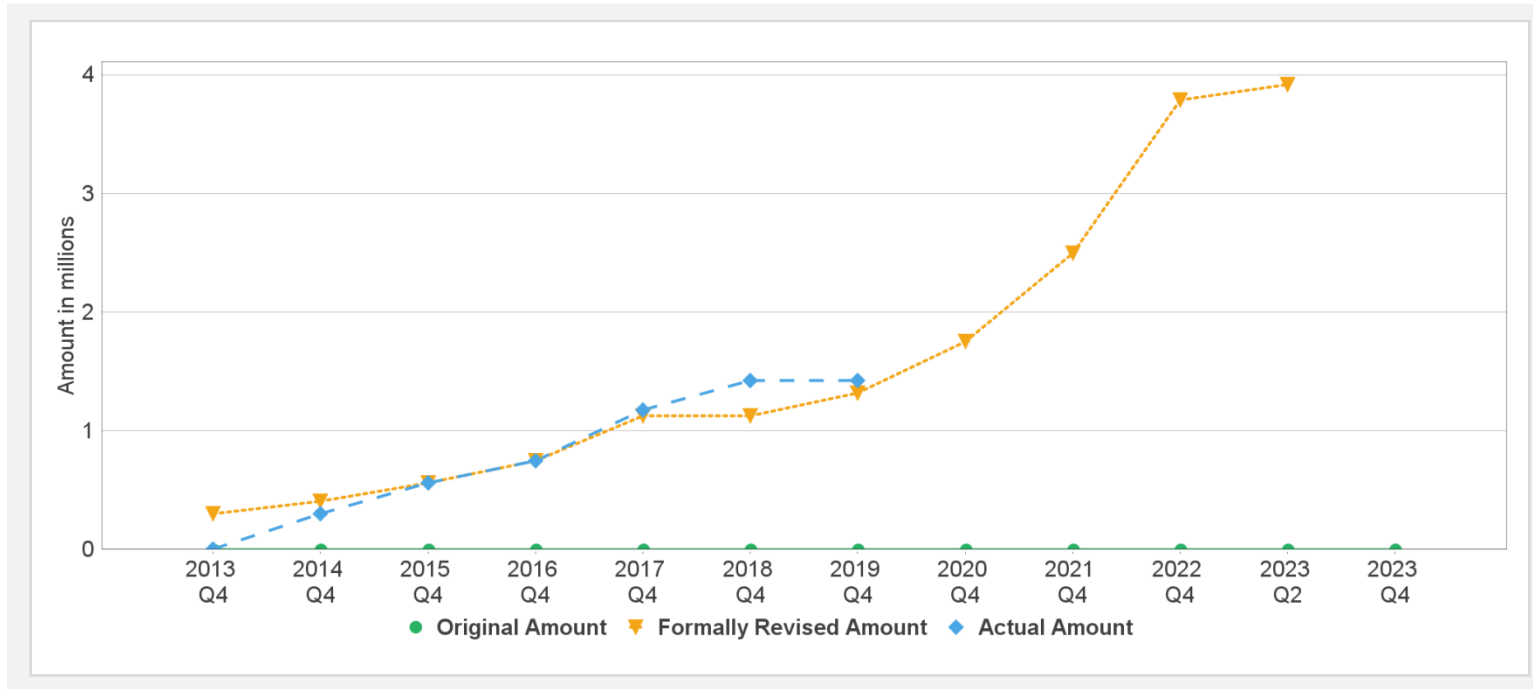

Restructuring History

Level 2 Approved on 27-Jun-2016

Related Project(s)

P160103-Jordan Ozone Depleting Substances HCFC Phase-Out (ODS3) Phase 2
