



Moldova Skills Data Capacity Building (P154573)

EUROPE AND CENTRAL ASIA | Moldova | Social Protection & Labor Global Practice |
Recipient Executed Activities | Investment Project Financing | FY 2016 | Seq No: 1 | ARCHIVED on 14-Jul-2017 | ISR29072 |

Implementing Agencies: Ministry of Labor, Social Protection and Family, Ministry of Finance

Key Dates

Key Project Dates

Bank Approval Date:23-Jun-2016

Effectiveness Date:27-Oct-2016

Original Closing Date:22-Sep-2018

Revised Closing Date:22-Sep-2018

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

To strengthen the Government of Moldova's capacity for evidence-based policymaking in the area of skills and employment through supporting enhanced collection and analysis of data on workforce skills and labor market needs

Has the Project Development Objective been changed since Board Approval of the Project Objective?

No

Components

Name

Overall Ratings

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	--	● Satisfactory
Overall Implementation Progress (IP)	--	● Satisfactory

Implementation Status and Key Decisions

The grant became effective on October 27, 2016, and since then implementation has been proceeding very quickly, particularly with respect to Component 1 (revised employer surveys). A new skills module was introduced into the existing employer survey (Labor Market Forecast Survey, LMFS) conducted by local National Employment Agency staff. The new module, designed specifically for Moldova and fielded in November 2016, enabled analysis of employers' perceptions of skills gaps in Moldova. At the same time, assessment of the existing instrument (LMFS) is being undertaken with a view to improve its usefulness in the future waves. With respect to Component 2 (surveys of working-age population on barriers to employment), the skills module for the household survey is currently being designed, with survey fielding expected in the fall. In terms of Component



3 (Capacity Building), discussions were held on the needs of each stakeholder in terms of STATA training envisioned under the grant and capacity was built by holding several working group meetings.

Risks

Overall Risk Rating

Risk Category	Rating at Approval	Previous Rating	Current Rating
Overall	--	--	● Moderate

Results

Project Development Objective Indicators

►Roadmap developed for improved collection, analysis, and dissemination of labor demand and supply data (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	N	Y
Date	04-Jul-2016	--	11-Jul-2017	30-Jun-2018

►Policy action plan developed for addressing skills mismatch (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	N	Y
Date	04-Jul-2016	--	11-Jul-2017	30-Jun-2018

Overall Comments

Intermediate Results Indicators



► Assessment of current data collection, analysis, and dissemination of labor demand (i.e. Labor Market Forecast Survey, LMFS) and recommendations how to increase its effectiveness (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	Ongoing	Y
Date	04-Jul-2016	--	11-Jul-2017	30-Jun-2018

► LMFS module developed to measure demand for cognitive and socio-emotional skills (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	Y	Y
Date	04-Jul-2016	--	10-Jul-2017	30-Jun-2017

► Dataset prepared containing the results of augmented LMFS (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	Y	Y
Date	04-Jul-2016	--	10-Jul-2017	30-Jun-2017

► Number of new modules developed on 1) supply of cognitive and socioemotional skills, and 2) barriers to employment (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	1.00	2.00
Date	04-Jul-2016	--	10-Jul-2017	30-Jun-2018



►Dataset prepared with new modules and labor market outcomes of resident working-age population (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	N	Y
Date	04-Jul-2016	--	11-Jul-2017	30-Jun-2018

►Number of staff trained in data analysis (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	20.00
Date	04-Jul-2016	--	11-Jul-2017	30-Jun-2018

►Analytical report on skills mismatches prepared (Text, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	N	Y
Date	04-Jul-2016	--	11-Jul-2017	30-Jun-2018

►Findings of skills mismatch analysis disseminated to the public (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	--	N	Y
Date	04-Jul-2016	--	11-Jul-2017	30-Jun-2018




►Number of meetings held by the Inter-Ministerial Project Working Group (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	5.00
Date	04-Jul-2016	--	--	30-Jun-2018

Overall Comments

Data on Financial Performance


Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P154573	TF-A2984	Effective	USD	0.30	0.30	0.00	0.05	0.26	 15%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P154573	TF-A2984	Effective	23-Jun-2016	22-Sep-2016	27-Oct-2016	22-Sep-2018	22-Sep-2018

Cumulative Disbursements

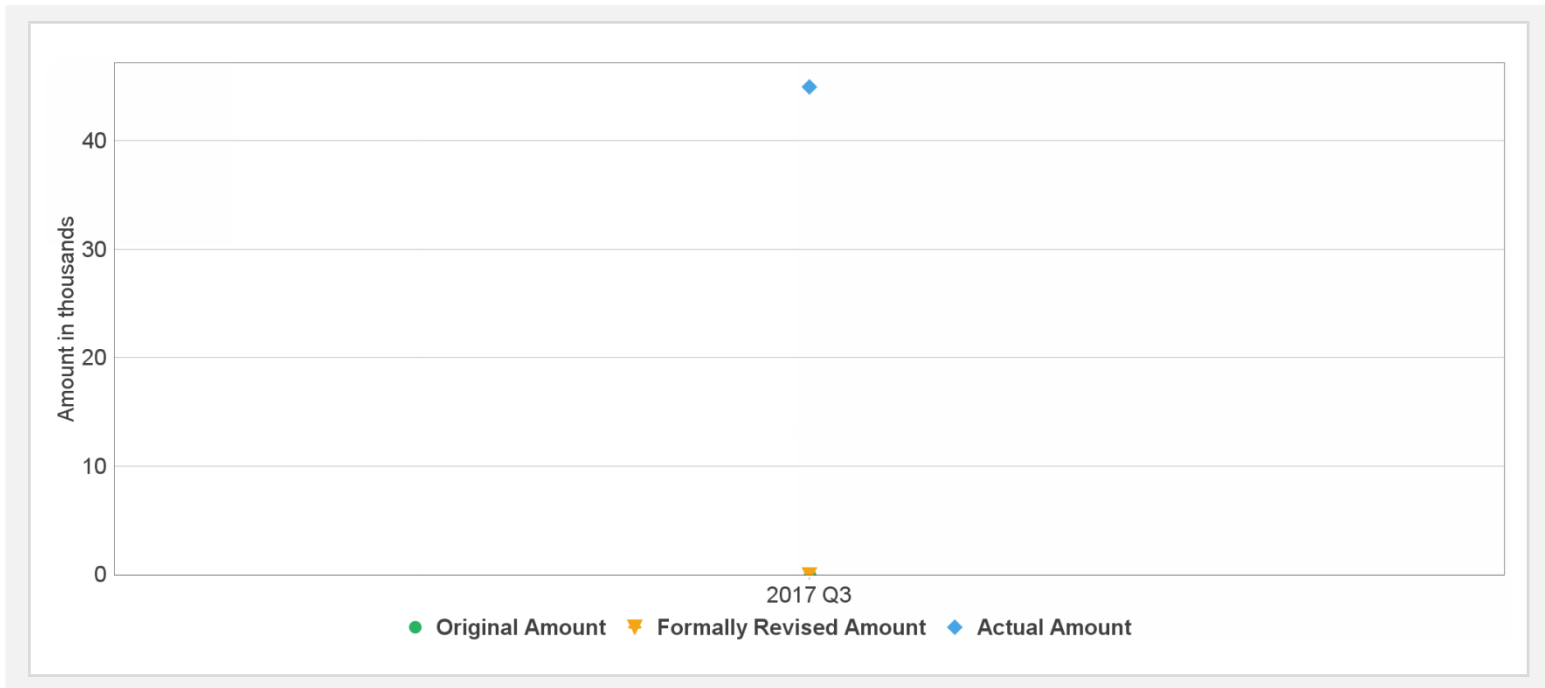

Restructuring History

There has been no restructuring to date.

Related Project(s)

There are no related projects.
