

Implementation Status & Results
Kyrgyz Republic
Capacity Building for Economic Management Grant (P108525)

Operation Name: Capacity Building for Economic Management Grant (P108525) Project Stage: Implementation Seq.No: 6 Status: ARCHIVED Archive Date: 12-Sep-2012

Country: Kyrgyz Republic Approval FY: 2009
 Product Line: IBRD/IDA Region: EUROPE AND CENTRAL ASIA Lending Instrument: Technical Assistance Loan
 Implementing Agency(ies): Ministry of Economic Regulation

Key Dates

Board Approval Date	01-Jul-2008	Original Closing Date	31-Dec-2012	Planned Mid Term Review Date	Last Archived ISR Date	26-Mar-2012
Effectiveness Date	18-Dec-2008	Revised Closing Date	31-Dec-2012	Actual Mid Term Review Date		

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The objective of the Project is to assist the Recipient in establishing and institutionalizing an efficient and effective framework for formulating and implementing sustainable economic policies as well as in enhancing the capacity of public institutions responsible for the development and implementation of such policies to formulate and carry out the policies. [Objective as reflected in the Financing Agreement, which in substance is not different from the PAD but wordings are different. The most important project objectives are: a) contribute to government-wide coherent macro-economic policy development and decision making through establishing strong inter-ministerial coordination and interface; b) support process of economic policy development and implementation through enabling public institutions (and particularly the MEDT, through capacity building and restructuring) to formulate sound and analytically informed policy measure and proposals; and c) support reform of employment practices and wages in the civil service by building the capacity in a special task force in this area. [These other main objectives are from the PAD but are not reflected in the legal agreement except item b. although broadly in line in substance]

Has the Project Development Objective been changed since Board Approval of the Project?

Yes No

Component(s)

Component Name	Component Cost
Institutional and Technical Framework for Macro-Economic Policy	0.50
Strengthening the Capacity to Formulate and Implement Economic Policy	1.64
Building Capacity for Civil Service Reform	0.34
Project Management and Implementation Support	0.33

Overall Ratings

	Previous Rating	Current Rating
Progress towards achievement of PDO	Moderately Satisfactory	Moderately Satisfactory
Overall Implementation Progress (IP)	Moderately Satisfactory	Moderately Satisfactory

	Previous Rating	Current Rating
Overall Risk Rating		

Implementation Status Overview

Two rounds of disruption in the government hindered project implementation. First, the government was restructured to a large extent in October 2009; among other changes, the "Central Agency on Development, Investment, and Innovation" (CADII) was established and empowered with competencies over most economic policy decisions, donor coordination, and all external assistance. These changes caused shifts in the role and responsibilities of the government agencies involved in the implementation of various components and sub-components of the project. The majority of competencies that belonged to the Ministry of Economic Development and Trade (MEDT)--originally the main implementation partner for CBEM--were shifted to CADII. Consequently, CADII became the main implementing agency for CBEM.

The second round of disruption was caused by the April and June events of 2010. The April 2010 political uprising forced the President to resign and led to the formation of an interim government headed by a coalition of opposition political and civic leaders. CADII was abolished. Then in June social tensions and inter-ethnic clashes broke out in the south of the country, disrupting the government's operations and implementation of many projects, including CBEM.

Subsequently, with the formation of the interim government in 2010, the primary responsibility for the implementation of the project (which had earlier moved from MEDT to CADII in October 2009) was shifted to the new Ministry of Economic Regulation, which has been assigned the majority of MEDT's competencies. Again, the government restructuring that took place at end-2011 resulted in renaming of the MER into the Ministry of Economy and Anti Monopoly Policy. The last round of government restructuring, however, did not hinder project implementation.

From early 2011, project implementation has accelerated significantly. However, due to significant initial delays and some capacity constraints, the implementation is still behind the original plan.

Locations

No Location data has been entered

Results

Project Development Objective Indicators

Public Disclosure Copy

Indicator Name	Core	Unit of Measure		Baseline	Current	End Target
Enhanced inter-ministerial coordination and capacity to ensure a coherent economic policy decision-making process.	<input type="checkbox"/>	Text	Value	No existing coordination in policy making across central Government. -date reflects Board date	The PM has signed a decree in June instituting regular monthly meetings of the Council. The Council met in July alongside a regular government meeting. Another separate meeting of the Council is planned for August.	High level coordination committee operational, holds regular meetings with relevant agenda for major economic policy decisions.
			Date	15-Jul-2008	16-Jul-2012	31-Dec-2012
			Comments		The next meeting of the Macroeconomic Policy Coordination Council is expected to be held in April 2012.	
Public institutions (and particularly the MEDT, through capacity building and restructuring) are enabled to formulate sound and analytically informed policy measure and proposals.	<input type="checkbox"/>	Text	Value	MEDT has old dysfunctional structure and low analytical capacity.	The structure of MEAMP has been changed, following among other things, the recommendations of the functional review. The analytical capacity within the ministry is still relatively weak and uneven across different units, but substantial progress in strengthening capacity has been made and continues to be made.	MER reorganized consistent with new structure.
			Date	15-Jul-2008	16-Jul-2012	31-Dec-2012
			Comments		Functional review prepared for reorganization of MEAMP (former MER). The process to reorganize MEAMP has not been completed. Policy Development Unit established and capacity of Macroeconomic and Fiscal Unit has been strengthened. Progress has also been made in strengthening MEAMP's capacity to carry out	

Public Disclosure Copy

					Regulatory Impact Assessments.	
Capacity for carrying out a reform of wages and employment in the civil service, together with options developed	<input type="checkbox"/>	Text	Value	No existing capacity to carry out a pay reform	End target has been fully met.	Salary task force presents options for wage and employment reform
			Date	15-Jul-2008	16-Jul-2012	31-Mar-2011
			Comments		Salary Task Force established and is fully functional.	

Intermediate Results Indicators

Indicator Name	Core	Unit of Measure		Baseline	Current	End Target
Presidential Decree/govt Regulation which (a) clearly defines roles & responsibilities in economic policy design, implementation & evaluation at central level (b) establishes an effective coordination	<input type="checkbox"/>	Text	Value	No coordination in economic policy	The coordination process has been formalized. At the technical level, an institutional structure has been developed to support the operations of the political level Macroeconomic Policy Coordination Council. Progress is being made in developing capacity at the technical level.	Coordination procedures formalized in decree or regulation. Agreement reached on composition and agenda of coordination committee
			Date	15-Jul-2008	16-Jul-2012	30-Jun-2011
			Comments			
Regular meetings of coordination group taking place, with appropriate agenda and relatively few major economic policy decisions being taken outside the mechanism.	<input type="checkbox"/>	Text	Value	No coordination in economic policy	The Prime Minister signed a decree in June instituting monthly meetings of the Macroeconomic Policy Coordination Council. The Council met in July alongside a regular government meeting. The Council is scheduled to meet again in August, as monthly meeting mandate has been introduced.	Coordination committee meeting regularly with substantive appropriate agenda.
			Date	15-Jul-2008	16-Jul-2012	31-Dec-2012
			Comments		The Council does not yet meet on a regular basis.	

Public Disclosure Copy

Publication of macroeconomic and fiscal forecasts with evidence that these forecasts provide the basis for budget and economic policy discussions.	<input type="checkbox"/>	Text	Value	Not currently published by Govt.	Forecasts are published twice a year on the website of MEAMP. The forecasts form the basis for the budget development process. However, the quality of the forecasts could be substantially improved.	Publication of more detailed forecasts at least twice during the year, and evidence that forecasts form the basis of budget planning.
			Date	15-Jul-2008	16-Jul-2012	31-Dec-2012
			Comments			
New structure of MEDT corresponds to that proposed in the SDP	<input type="checkbox"/>	Text	Value	Dysfunctional current structure		MEAMP reorganized consistent with new structure
			Date	15-Jul-2008	08-Mar-2012	31-Dec-2012
			Comments		Functional review of MER was completed. The restructuring process started, but is not complete yet. The new Minister has expressed his commitment to this process.	
Satisfactory implementation (according to private sector surveys) of significant measures to improve the business environment proposed by the investment council.	<input type="checkbox"/>	Text	Value	No specific survey to measure reforms proposed by the investment council.		Surveys indicate progress in other areas of business environment and increase satisfaction with the performance of IC and MEDT.
			Date	15-Jul-2008	08-Mar-2012	31-Dec-2012
			Comments		Despite the team's insistence, there was no readiness to launch the survey. However, the new government is taking significant steps to improve the business environment, which would probably reflect well on the results of a survey if the new Minister decides to conduct it.	
High quality policy papers are produced and subsequently translated into policy decisions.	<input type="checkbox"/>	Text	Value	No policy papers		At least six policy papers developed, of which three are judged to be of high quality and at least one forms the basis of a significant policy decision

Public Disclosure Copy

			Date	15-Jul-2008	08-Mar-2012	31-Dec-2012
			Comments		Two more policy papers are expected to be launched within the next month.	
Pay and grading reform group established	<input type="checkbox"/>	Text	Value	No existing taskforce		Salary task force established and basic data collected
			Date	15-Jul-2008	08-Mar-2012	31-Jul-2010
			Comments		Staffing of the Salary Task Force is 100% complete.	
Options paper for pay reform is produced	<input type="checkbox"/>	Text	Value	No current options for pay reform		Salary task force presents options for wage and employment reform
			Date	15-Jul-2008	08-Mar-2012	31-Dec-2010
			Comments			

Data on Financial Performance (as of 23-Aug-2012)


Financial Agreement(s) Key Dates

Project	Ln/Cr/Tf	Status	Approval Date	Signing Date	Effectiveness Date	Original Closing Date	Revised Closing Date
P108525	IDA-H3880	Effective	01-Jul-2008	22-Sep-2008	18-Dec-2008	31-Dec-2012	31-Dec-2012

Disbursements (in Millions)

Project	Ln/Cr/Tf	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P108525	IDA-H3880	Effective	XDR	1.90	1.90	0.00	0.90	1.00	47.00

Disbursement Graph

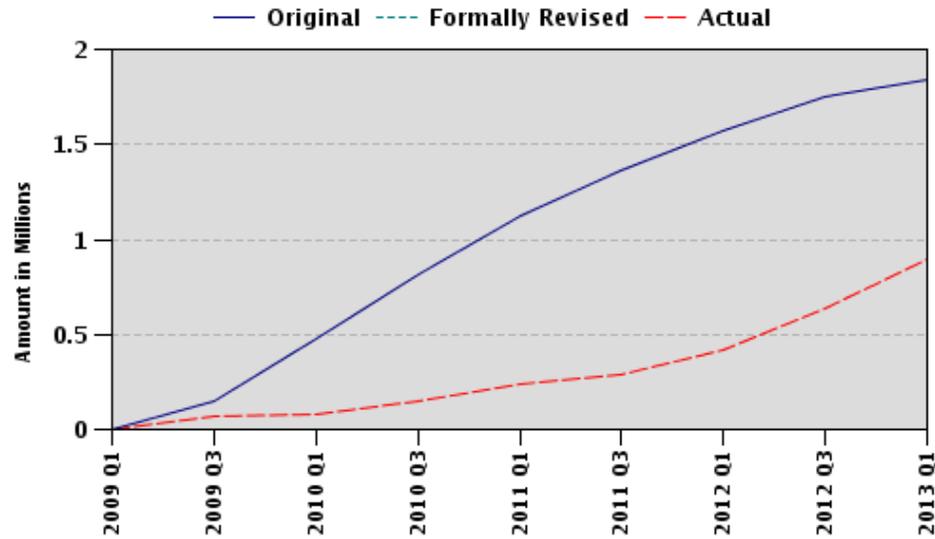

Key Decisions Regarding Implementation

Several important decisions were made following the appointment of the interim government in April 2010 and the formation of a new government after the October 2010 elections. First, the project Steering Committee (SC)--the project oversight body with representation from government agencies involved in CBEM implementation--that had previously been disbanded--was reappointed and re-assigned the roles and responsibilities of leading and managing the project components. Second, more power was given to the heads of individual components within the SC to independently make decisions specifically related to the implementation of their respective project components. Third, the procurement plan was revised, allocating more funds to the activities where implementation progress was faster and additional funding was needed. Finally, a local Project Manager with the mandate to facilitate project implementation was hired in 2011. The Project Manager resigned in May 2012, but a new one has been appointed in July. These decisions have had a positive effect on project implementation.

Restructuring History

Level two Approved on 14-Nov-2011

Related Projects

There are no related projects.
