Public Disclosure Authorized
Public Disclosure Copy

Implementation Status & Results
India
Bihar Rural Livelihoods Project - "JEEViKA" (P090764)

Operation Name: Bihar Rural Livelihoods Project - "JEEViKA" (P090764) | Project Stage: Implementation | Seq.No: 15 | Status: ARCHIVED | Archive Date: 02-Dec-2014

Country: India | Approval FY: 2007

Product Line: IBRD/IDA | Region: SOUTH ASIA | Lending Instrument: Specific Investment Loan

Implementing Agency(ies): Bihar Rural Livelihoods Promotion Society

Key Dates

Board Approval Date	14-Jun-2007	Original Closing Date	31-Oct-2012	Planned Mid Term Review Date	21-Jun-2011	Last Archived ISR Date	23-May-2014
Effectiveness Date	01-Oct-2007	Revised Closing Date	31-Oct-2015	Actual Mid Term Review Date	05-Aug-2012		

Project Development Objectives

Project Development Objective (from Project Appraisal Document)

The project development objective is to enhance social and economic empowerment of the rural poor in Bihar.

Has the Project Development Objective been changed since Board Approval of the Project?

○ Yes ◉ No

Component(s)

Component Name	Component Cost
Community Institution Development	56.80
Community Investment Fund	142.00
Technical Assistance Fund	18.10
Project Management	18.90

Overall Ratings

	Previous Rating	Current Rating
Progress towards achievement of PDO	Satisfactory	Satisfactory
Overall Implementation Progress (IP)	Satisfactory	Moderately Satisfactory
Overall Risk Rating	Moderate	Moderate

Implementation Status Overview

In the last six months, the project has scaled up both mobilization and capitalization of the community institutions. The project has thus far mobilized 1,220,000 households into 102,000 self -help groups and federations. These households have mobilized US$10 million of savings and US$60 million of financing from commercial banks. The project is on track to achieve results envisaged for mobilization and capitalization.

Public Disclosure Copy

As part of deepening livelihood interventions, the project has mobilized nearly 1000 producer organizations including nearly 55,000 households across agriculture, dairy and poultry sectors. The project has also initiated the financing of the producer organizations and nearly 50 producer organizations have been financed till date. The back yard poultry intervention has been scaled up to nearly 30,000 households. The project has also expanded the community managed health and nutrition centers adding 50 more centers in last six months.

In September, Bill and Melinda Gates Foundation (BMGF) have decided to scale up their existing partnership with JEEViKA to deepen the nutrition, health and food security interventions in the project. The partnership will help JEEViKA in introducing and scaling up health, nutrition and food security interventions in a majority of the SHGs that have been mobilized till date.

Locations

Country	First Administrative Division	Location	Planned	Actual
India	State of Bihar	Wazirganj		
India	State of Bihar	Tankuppa		
India	State of Bihar	Sherghati		
India	State of Bihar	Sarmera		
India	State of Bihar	Sakri		
India	State of Bihar	Rajnagar		
India	State of Bihar	Rajgir		
India	State of Bihar	Purnia		
India	State of Bihar	Pandaul		
India	State of Bihar	Nalanda		
India	State of Bihar	Nagar Nahusa		
India	State of Bihar	Muzaffarpur		
India	State of Bihar	Mushari		
India	State of Bihar	Manpur		
India	State of Bihar	Madhubani		
India	State of Bihar	Lakhaura		
India	State of Bihar	Kurhani		
India	State of Bihar	Kothia		
India	State of Bihar	Khizr Sarai		

Public Disclosure Copy

Public Disclosure Copy

Country	First Administrative Division	Location	Planned	Actual
India	State of Bihar	Khagaul		
India	State of Bihar	Jhanjharpur		
India	State of Bihar	Jainagar		
India	State of Bihar	Harnaut		
India	State of Bihar	Gurua		
India	State of Bihar	Gaya		
India	State of Bihar	Dobhi		
India	State of Bihar	Dhamdaha		
India	State of Bihar	Chautham		
India	State of Bihar	Bodh Gaya		
India	State of Bihar	State of Bihar		
India	State of Bihar	Bihar Sharif		
India	State of Bihar	Benipati		
India	State of Bihar	Barachati		
India	State of Bihar	Banmankhi		
India	State of Bihar	Baisi		
India	State of Bihar	Asthanwan		
India	State of Bihar	Amour		
India	State of Bihar	Amas		
India	State of Bihar	Bhawanipur		
India	State of Bihar	Khagaria		
India	State of Bihar	Khagaria		
India	State of Bihar	Minapur		
India	State of Bihar	Saraiya		
India	State of Bihar	Rupauli		

Public Disclosure Copy

Public Disclosure Copy

Results

Project Development Objective Indicators

Indicator Name	Core	Unit of Measure		Baseline	Current	End Target
Self managed self help groups established, covering at least 80% of the target households.	☐	Text	Value	0	102,000 SHGs covering 1,220,000 households	150,000 SHGs covering 1,500,000 target housholds
			Date	15-Oct-2007	01-Oct-2014	30-Sep-2015
			Comments		On track.	
At least 50% of those who have received CIF have increased income by at least 30% of the baseline.	☐	Text	Value	0	Not available at this stage. Will be available by march	50% of the households receiving CIF increase income by 30%
			Date	15-Oct-2007	01-Oct-2014	30-Sep-2015
			Comments			

Intermediate Results Indicators

Indicator Name	Core	Unit of Measure		Baseline	Current	End Target
Intended beneficiaries aware of project info. and project investments (%)	☒	Percentage	Value	0.00	90.00	100.00
			Date	15-Oct-2007	01-Oct-2014	30-Sep-2015
			Comments			
Intended beneficiaries aware of project info. and project investments - female	☒	Number Sub Type Supplemental	Value	0.00	1220000.00	1500000.00
Intended beneficiaries aware of project info. and project investments –male	☒	Number Sub Type Supplemental	Value	0.00	1100000.00	1500000.00
Intended beneficiaries - female (number)	☒	Number Sub Type Supplemental	Value	0.00	1220000.00	1500000.00
Intended beneficiaries - male (number)	☒	Number Sub Type Supplemental	Value	0.00	1100000.00	1500000.00
At least $11.9 million benefeciary savings mobilized leveraging $17.8 million of financial institution lending and $23.8 million inter loaning by the end of the project.	☐	Text	Value	0	$10 million Savings and $60 million lending	$ 11.9 million (saving), $ 42 million (lending)
			Date	15-Oct-2007	01-Oct-2014	30-Sep-2015
			Comments		on track. likely to exceed the values for end targets	

Public Disclosure Copy

Public Disclosure Copy

No. of targatted poor households that are organised into SHGs represented in VO and BLF	☐	Number	Value	0.00	1100000.00	1500000.00
			Date		01-Oct-2014	30-Sep-2015
			Comments		On track	

Data on Financial Performance (as of 10-Nov-2014)

Financial Agreement(s) Key Dates

Project	Ln/Cr/Tf	Status	Approval Date	Signing Date	Effectiveness Date	Original Closing Date	Revised Closing Date
P090764	IDA-43230	Effective	14-Jun-2007	09-Aug-2007	01-Oct-2007	31-Oct-2012	31-Oct-2015
P090764	IDA-51230	Effective	31-May-2012	09-Jul-2012	05-Sep-2012	31-Oct-2015	31-Oct-2015

Disbursements (in Millions)

Project	Ln/Cr/Tf	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
P090764	IDA-43230	Effective	XDR	41.40	41.40	0.00	41.40	0.00	100.00
P090764	IDA-51230	Effective	XDR	64.60	64.60	0.00	22.22	42.38	34.00

Disbursement Graph

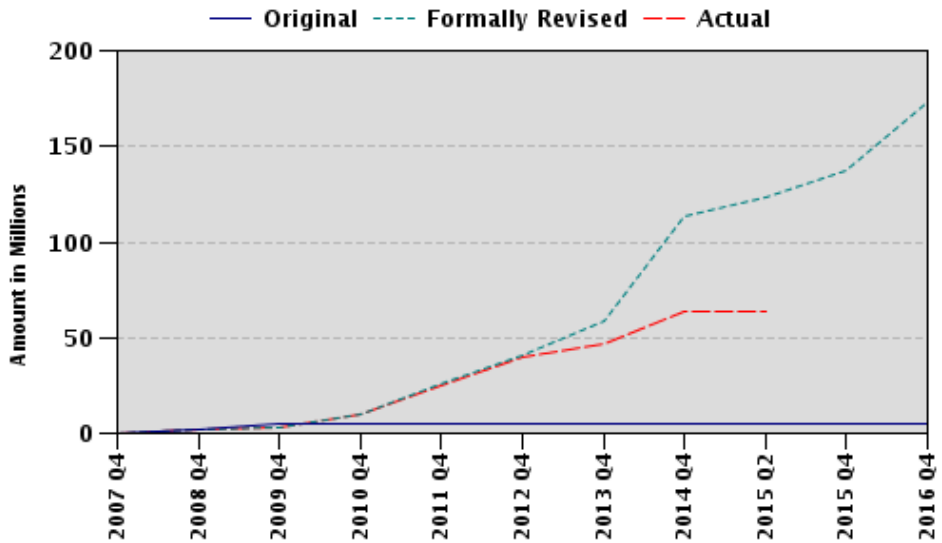

Key Decisions Regarding Implementation

A detailed implementation support mission will be undertaken in end December, 2014. The mission will focus on reviewing overall status of implementation progress including the

Public Disclosure Copy

disbursement status, status of the financing of the producer organizations and the status of the partnerships with the agencies identified through the Bihar Innovation Forum II. The mission will also review performance of various project management systems. The ISR will again be updated in January based on the findings of the implementation support mission.

Restructuring History

There has been no restructuring to date.

Related Projects

P130546-Bihar Rural Livelihood Project Additional Financing

Public Disclosure Copy

Public Disclosure Copy
