Public Disclosure Copy

Public Disclosure Authorized

India: Andhra Pradesh Rural Inclusive Growth Project (P152210)

SOUTH ASIA | India | Agriculture Global Practice |
IBRD/IDA | Investment Project Financing | FY 2015 | Seq No: 7 | ARCHIVED on 08-Mar-2018 | ISR31291 |

Implementing Agencies: Society for Elimination of Rural Poverty, Department of Economic Affairs, Ministry of Finance

Key Dates

Key Project Dates

Bank Approval Date:19-Dec-2014
Effectiveness Date:02-Feb-2016
Planned Mid Term Review Date:28-May-2018
Actual Mid-Term Review Date:--
Original Closing Date:30-Jun-2020
Revised Closing Date:30-Jun-2020

Project Development Objectives

Project Development Objective (from Project Appraisal Document)
The PDO is to enable selected poor households to enhance agricultural incomes and secure increased access to human development services and social entitlements.

The “selected poor households” will include households that are geographically & socially excluded and have low income levels. The incomes for these households will be enhanced by ensuring increased incomes from agriculture andallied sectors through increased productivity and enhanced market access. The “human developmentservices” include services relatedto health, nutrition and sanitation. The “social entitlements” mainly include social safety nets like the wages from National RuralEmployment Guarantee Scheme, pensions and insurance benefits that are provided by the government.

Has the Project Development Objective been changed since Board Approval of the Project Objective?
No

Components

Name
Value Chain Development:(Cost $44.00 M)
Human Development:(Cost $19.00 M)
Access to Social Protection Services & Entitlements:(Cost $13.00 M)
Mission Support, ICT and Partnerships:(Cost $20.00 M)
Project Implementation Support:(Cost $11.00 M)

Overall Ratings

Public Disclosure Copy

Public Disclosure Copy

Name	Previous Rating	Current Rating
Progress towards achievement of PDO	Moderately Satisfactory	Moderately Satisfactory
Overall Implementation Progress (IP)	Moderately Satisfactory	Moderately Satisfactory
Overall Risk Rating	Substantial	Substantial

Implementation Status and Key Decisions

The project is structured into 3 key program Components a) Value Chain Development: focusing on improving incomes of 250,000 small and marginal farmers by at least 50%; b) Human Development: aimed at improving health, nutrition and sanitation behaviors of 250,000 poor households and c) Access to Social Protection Services and Entitlements: with an objective to improve coverage and service delivery of social protection entitlements of 500,000 of poorest households.

The project made considerable physical progress across several components during last six months, viz. (a) More than 255,000 farmers have been mobilized under 22,000 Farmer Producer Groups (FPGs) and 162 Farmer Producer Organizations (FPOs) for agriculture/horticulture and animal husbandry activities; The project has planned to scale up cashew marketing through Olam and few other commodities. (b) 3,352 Village Marts (member of 71 Mandal Nodal Stores) across 13 districts are functioning with reasonably good turnover; (c) Health sub-committees in 5,400 Gram Panchayats (GP) (out of the 6,196 GPs) have been trained for supporting the Human Development goals; (d) More than 67 thousand families are maintaining nutrition gardens and nearly 60 thousand families are rearing backyard poultry, for improved access to nutrition; (e) 133 One Stop Shops (OSS) with 61 having full bundle of services are operational. Additionally, another 167 locations have been identified in Integrated Tribal Development Agency (ITDA) areas.

The intervention areas, in all the components, need further deepening with market based approaches and good practices. This is critical to ensure post project sustainability of the new institutions developed. The Farmer Producer Group (FPG) formation in the existing Project villages needs to be intensified, along with pursuance of active handholding and continued strengthening of the FPGs and the Farmer Producer Organizations. Towards this, the Project needs to strengthen core staffing to support emerging technical needs.

Public Disclosure Copy

Public Disclosure Copy

Public Disclosure Copy

Public Disclosure Copy

Public Disclosure Copy

Risks

Systematic Operations Risk-rating Tool

Risk Category	Rating at Approval	Previous Rating	Current Rating
Political and Governance	--	Low	Low
Macroeconomic	--	Low	Low
Sector Strategies and Policies	--	Low	Low
Technical Design of Project or Program	--	Substantial	Substantial
Institutional Capacity for Implementation and Sustainability	--	Substantial	Substantial
Fiduciary	--	Moderate	Moderate
Environment and Social	--	Moderate	Moderate
Stakeholders	--	Moderate	Moderate
Other	--	--	--
Overall	--	Substantial	Substantial

Results

Project Development Objective Indicators

▸ 50% incremental income increase of the target households (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	50.00
Date	31-Dec-2014	30-Jun-2017	07-Feb-2018	30-Jun-2020

▸ 70% of the producers benefitting are from poorest and SC/ST households (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	89.00	91.00	70.00

Date	19-Dec-2014	30-Jun-2017	07-Feb-2018	30-Jun-2020

▸ % increase in pregnant and lactating women who practise core child nutrition and health care behaviours (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	70.00
Date	19-Dec-2014	30-Jun-2017	07-Feb-2018	30-Jun-2020

▸ Where one stop shop has been established % of eligible households with access to at least 3 entitlement programs or key services (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	0.00	80.00
Date	31-Dec-2014	30-Jun-2017	07-Feb-2018	30-Jun-2020

Overall Comments

Intermediate Results Indicators

▸ % of targeted households organized into producer organisations (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	85.00	100.00	70.00
Date	19-Dec-2014	31-Aug-2017	07-Feb-2018	30-Jun-2020

▸ % increase in productivity from improved agriculture practices (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	30.00
Date	19-Dec-2014	23-Nov-2016	07-Feb-2018	30-Jun-2020

▸ % increase in per unit price realization (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	0.00
Date	19-Dec-2014	23-Nov-2016	07-Feb-2018	30-Jun-2020

▸ % increase in quality and size of consumer baskets purchased at KRuSHE mart (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	40.00
Date	19-Dec-2014	23-Nov-2016	07-Feb-2018	30-Jun-2020

▸ % of villages in the target mandals that have prepared and are implementing village HD/WASH plans (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	100.00	100.00	90.00
Date	19-Dec-2014	31-Aug-2017	07-Feb-2018	30-Jun-2020

Public Disclosure Copy

▸ % of exception reports generated by the mother and child tracking system acted upon by the field functionaries (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	95.00
Date	19-Dec-2014	--	07-Feb-2018	30-Jun-2020

▸ % of villages reporting data in the integrated mother and child tracking system (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	95.00
Date	19-Dec-2014	--	07-Feb-2018	30-Jun-2020

▸ number of VHNSC , PRI members and field functionaries of the line depts trained (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	10,000.00
Date	19-Dec-2014	--	07-Feb-2018	30-Jun-2020

▸ No of targeted panchayats that have operationalized one stop shop services for saftey nets and entitlements (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	133.00	133.00	1,000.00
Date	19-Dec-2014	31-Aug-2017	07-Feb-2018	30-Jun-2020

Public Disclosure Copy

Public Disclosure Copy

▸ % of enrolled beneficiaries in targeted gram panchayats who receive payments on time for key entitlements (NREGA, Social pensions, insurance) (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	80.00
Date	19-Dec-2014	--	07-Feb-2018	30-Jun-2020

▸ Extent of utlisation of ICT for measurement and decision support (index to be developed) (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	80.00
Date	19-Dec-2014	--	07-Feb-2018	30-Jun-2020

▸ Number of good quality technical support agencies working with the project (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	5.00	4.00	8.00
Date	19-Dec-2014	31-Aug-2016	07-Feb-2018	30-Jun-2020

▸ Number of partners working with the project in providing market access for producers (Number, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	8.00	8.00	8.00
Date	19-Dec-2014	31-Aug-2017	07-Feb-2018	30-Jun-2020

Public Disclosure Copy

Public Disclosure Copy

▸ Project Monitoring, Evaluation and lLearning (M, E and L) System including MIS established (Yes/No, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	N	Y	N	Y
Date	19-Dec-2014	31-Aug-2017	07-Feb-2018	30-Jun-2020

▸ Project implementation prcedures and agreed business standards are followed for atleast 80% of the project interventions (Percentage, Custom)

	Baseline	Actual (Previous)	Actual (Current)	End Target
Value	0.00	--	--	80.00
Date	19-Dec-2014	--	07-Feb-2018	30-Jun-2020

Overall Comments

Data on Financial Performance

Disbursements (by loan)

Project	Loan/Credit/TF	Status	Currency	Original	Revised	Cancelled	Disbursed	Undisbursed	Disbursed
P152210	IDA-55760	Effective	USD	75.00	75.00	0.00	20.61	54.39	27%

Key Dates (by loan)

Project	Loan/Credit/TF	Status	Approval Date	Signing Date	Effectiveness Date	Orig. Closing Date	Rev. Closing Date
P152210	IDA-55760	Effective	19-Dec-2014	16-Nov-2015	02-Feb-2016	30-Jun-2020	30-Jun-2020

Cumulative Disbursements

Public Disclosure Copy

Public Disclosure Copy

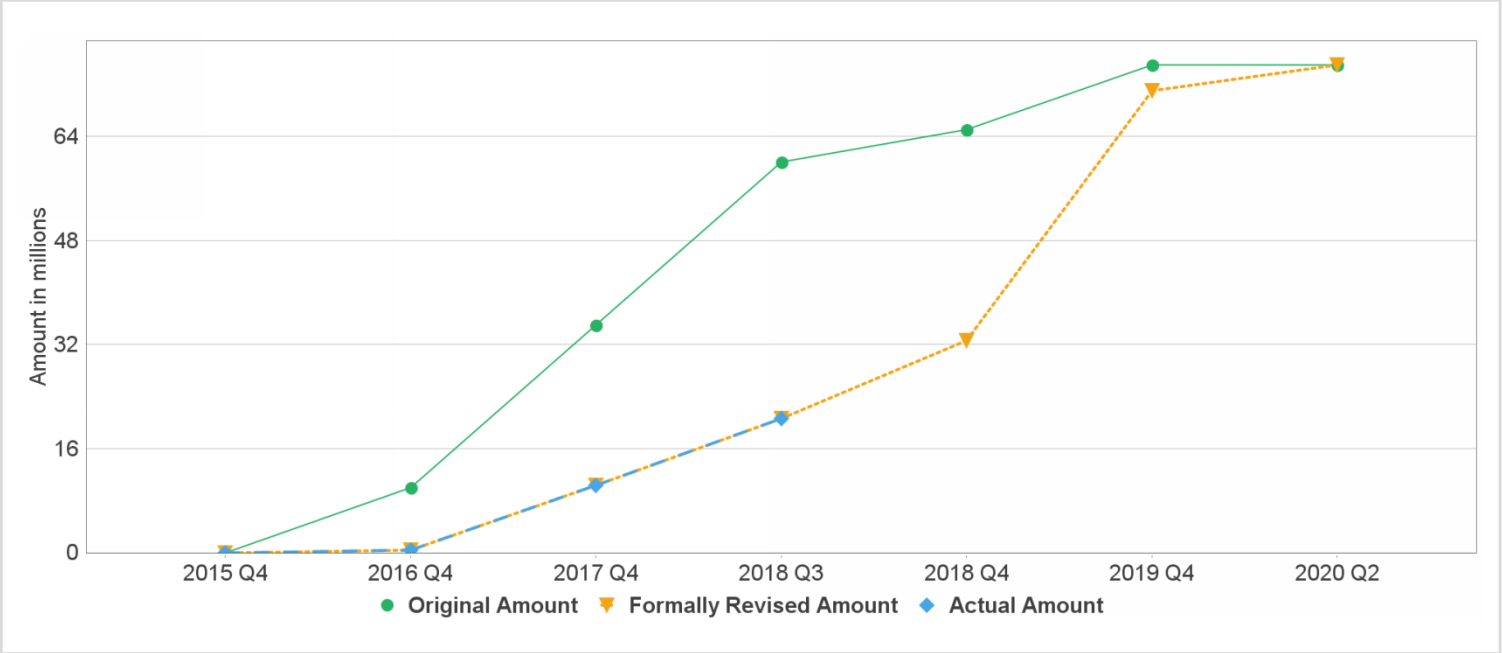

Restructuring History

Level Approved on 22-Sep-2015

Related Project(s)

There are no related projects.

Public Disclosure Copy
